


construction intelligence®

EPIC for Modification & Improvement Works to NGL Complex Buildings

Mesaieed, Qatar

Overview



Reference No : PRJQA19171382

Project Sector : Oil & Gas

Project Industry : Oil & Gas Infrastructure

Project Type : Offsites & Utilities

Stage : Under Construction

Completion % : 29%

Est. Project Value 1 : \$ 16.0 million

Last Updated : Jun 2, 2023

Created On : May 22, 2019

Description

The project involves the modification and improvement work at NGL Complex, Mesaieed. The scope of works includes engineering, procurement, installation & commissioning of modification and improvement works to the existing occupied buildings at NGL Complex, Mesaieed.

The project will include:

- Conversion of buildings Nos. 7 & 9 into a new NGL Laboratory
- Installation of Toxic and Flammable Gas Detectors at all occupied buildings
- Modification of the buildings HVAC systems to close the fresh air intakes on the detection of gas
- Upgradation of buildings to meet current building and safety codes and regulations and to meet the safe haven standard.

Project News and Updates

Date	Туре	Added By	News & Updates
Jun 1, 2023	Note	BNC	Sources closely associated with the project have confirmed that the construction works are underway.
Feb 20, 2023	Note	BNC	The companies associated with the project have confirmed that the project is in progress. We are yet to identify the MEP contractor & Consultant details and shall update the record as soon as we receive this information.
Sep 15, 2022	Note	BNC	We have currently paused the tracking of Qatar construction projects in accordance with the stoppage of construction work during the FIFA 2022 tournament. Project tracking on this project is scheduled to resume in January, 2023.
Jul 27, 2022	Note	BNC	As per recent updates, Petroserv Limited WLL has won an EPIC contract from Qatar Energy for the modification and improvement of works to the existing occupied buildings at NGL Complex. The contract is valued at USD 14.87 million (QR 54.16 million). The project will be completed on January 31, 2024. We have not been able to identify the FEED consultant so far and will update this record as soon as we have this information available.
Jul 14, 2022	Note	BNC	As per recent updates, the project is still in the tender stage and the contractor is yet to be appointed.
Jun 9, 2022	Note	BNC	Industry sources suggest that the bid evaluation is still in progress.
			Recent sources suggest that the main construction COPYRIGHT © 2023, Industry Networks FZC.

(00) Bito. El lo la mamadan a improvement violte la riole della manage				
May 11, 2022	Note	BNC	contract has not been awarded yet.	
Apr 18, 2022	Note	BNC	As per recent updates, the tender to award the main construction contract is still under evaluation.	
Mar 16, 2022	Note	BNC	Based on recent sources, it is understood that the main contractor has not been finalized. Direct confirmation from the project owner is yet to be obtained.	
Feb 28, 2022	Note	BNC	Based on recent sources, the project is understood to be under evaluation. We have not received direct confirmation from the project owner and shall update this record once further information is availed.	

Schedules

Note: The construction industry is very dynamic and project schedules are subject to constant change. The schedule listed here is estimated based on feedback received by us when the project was last updated.

ilsted here is estimated based on recaback received by as when the project was last apaated.					
Jan 2021	Main Consultant Award Date	Estimated			
Oct 2021	Main Contractor Tender Announce Date	Estimated			
Dec, 26 2021	Main Contractor Bid Closing Date	Estimated			
Jul 2022	Main Contractor Award Date	Estimated			
Jan 2024	Completion Date	Estimated			

Companies (2)

Owner(s) (1)

Qatar Energy (formerly Qatar Petroleum)

Location : Doha, Qatar

Role : Government Owner

Office No. :

Website : https://www.qatarenergy.qa/en/Pages/Home.aspx

Contractor(s) (1)

▶ Other Contractors - awarded (1)

Petrosery Limited WLL

Status : Won

Location : Doha, Qatar

Role : Engineering, Procurement, Construction & Installation (EPCI)

Contractor


: Mr. Rathinakumar Balasubraman

Office No. (Project Manager)
+974-4-4190333


Website : http://www.petroserv-limited.com/

Award Date : 2022-07-25 Award Value : 14.88 million

Estimated Percentage Completion

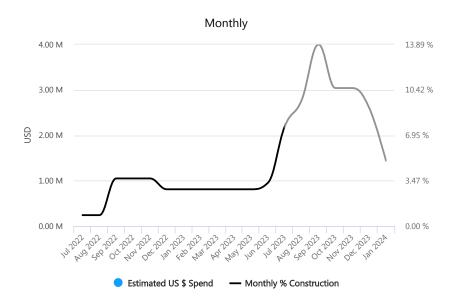

Estimated Spend Forecast

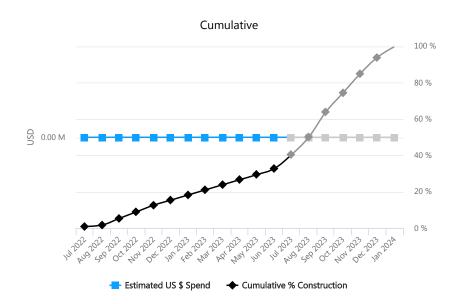

Completed

Completed

Forecasted

Forecasted

The monthly and cumulative "estimated percentage completion and spend" graphs are calculated using a series of algorithms that have been specifically developed for each project type, in consultation with leading engineering consultants and contractors. Due

to the specific and unique considerations on a project and the dynamic nature of construction the above graphs may at times vary from the actual progress at the site.

DISCLAIMER

The information, content and documents from or through BNC are provided "as-is," "as available," with "all faults", and all warranties, express or implied, are disclaimed (including but not limited to the disclaimer of any implied warranties of merchantability and fitness for a particular purpose). We and our affiliated parties have no liability whatsoever for your use of any information, except as provided in our Terms of Service. In particular, but not as a limitation thereof, we and our affiliated parties are not liable for any indirect, special, incidental or consequential damages (including damages for loss of business, loss of profits, litigation, or the like), whether based on breach of contract, breach of warranty, tort (including negligence), product liability or otherwise, even if advised of the possibility of such damages. The negation and limitation of damages set forth above are fundamental elements of the basis of the bargain between us and you. This product, services, documents and information presented would not be provided without such limitations. No advice or information, whether oral or written, obtained by you from us through BNC or otherwise shall create any warranty, representation or guarantee.

COPYRIGHT © 2023, Industry Networks FZC. The content, organization, graphics, design, compilation, magnetic translation, digital conversion and other matters related to BNC are protected under applicable copyrights, trademarks and other proprietary (including but not limited to intellectual property) rights. The copying, redistribution, use or publication of any such matters or any part of BNC, is strictly prohibited.
